




Project: BSA_SchedulePhase1_R
 Date: Mon 4/24/23

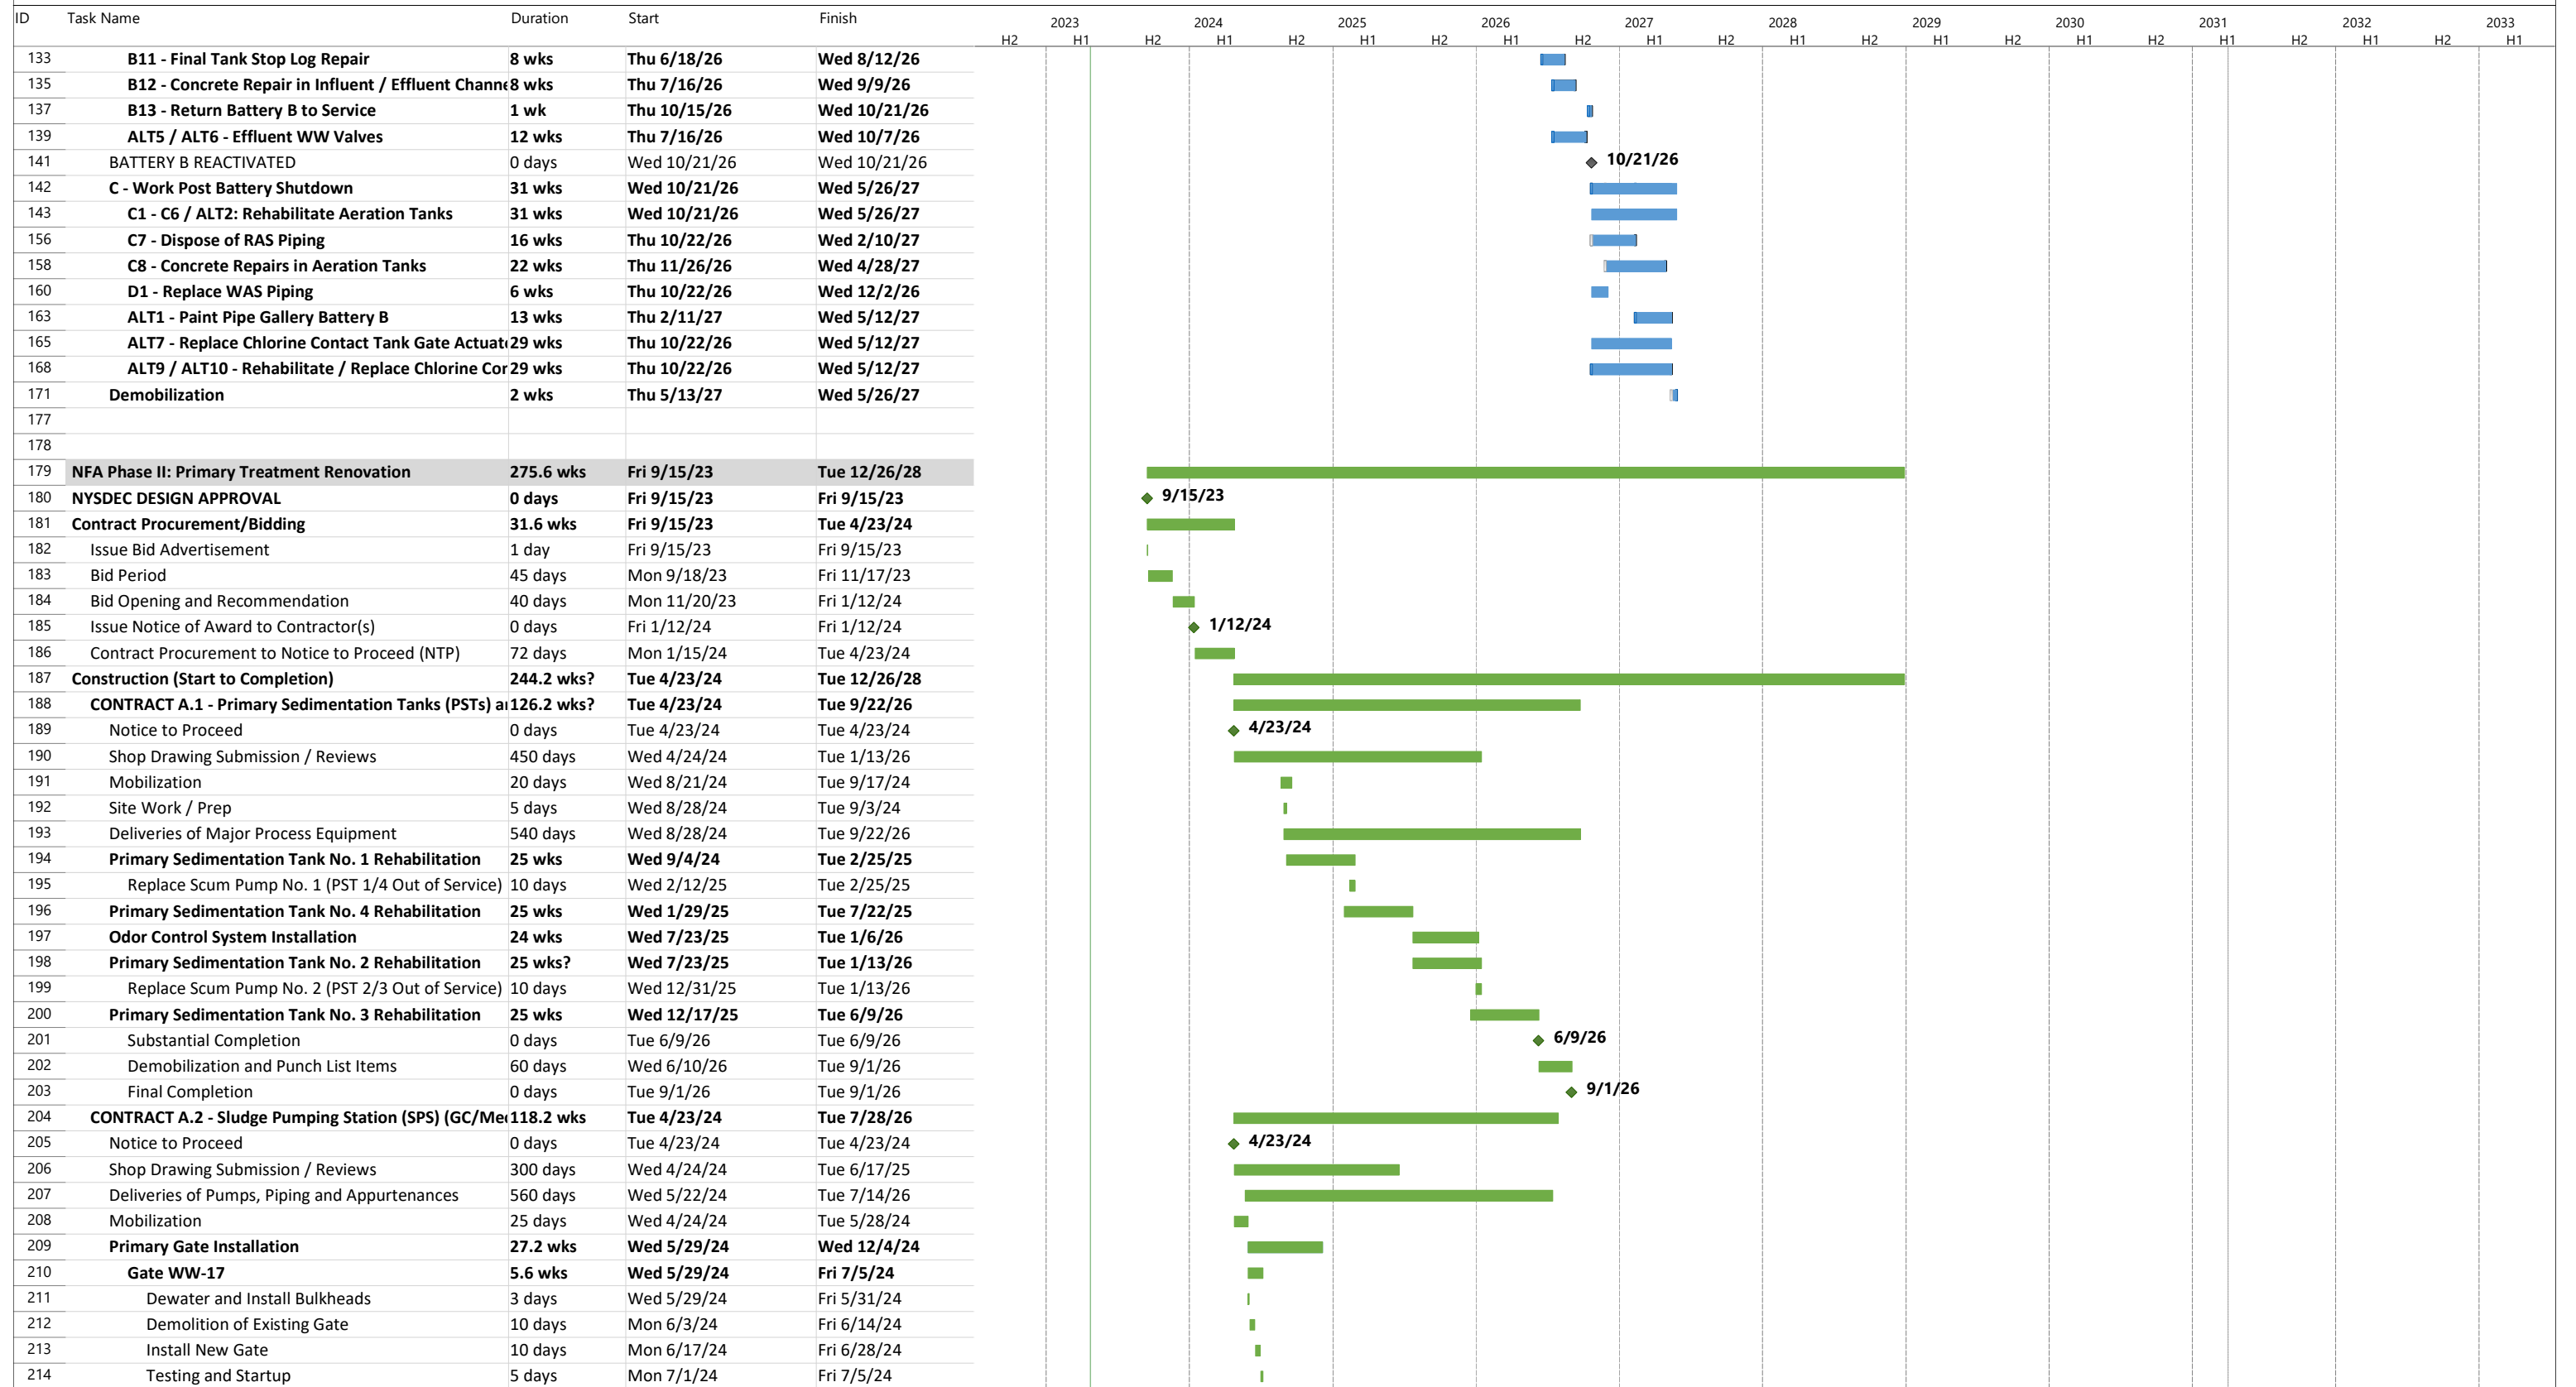


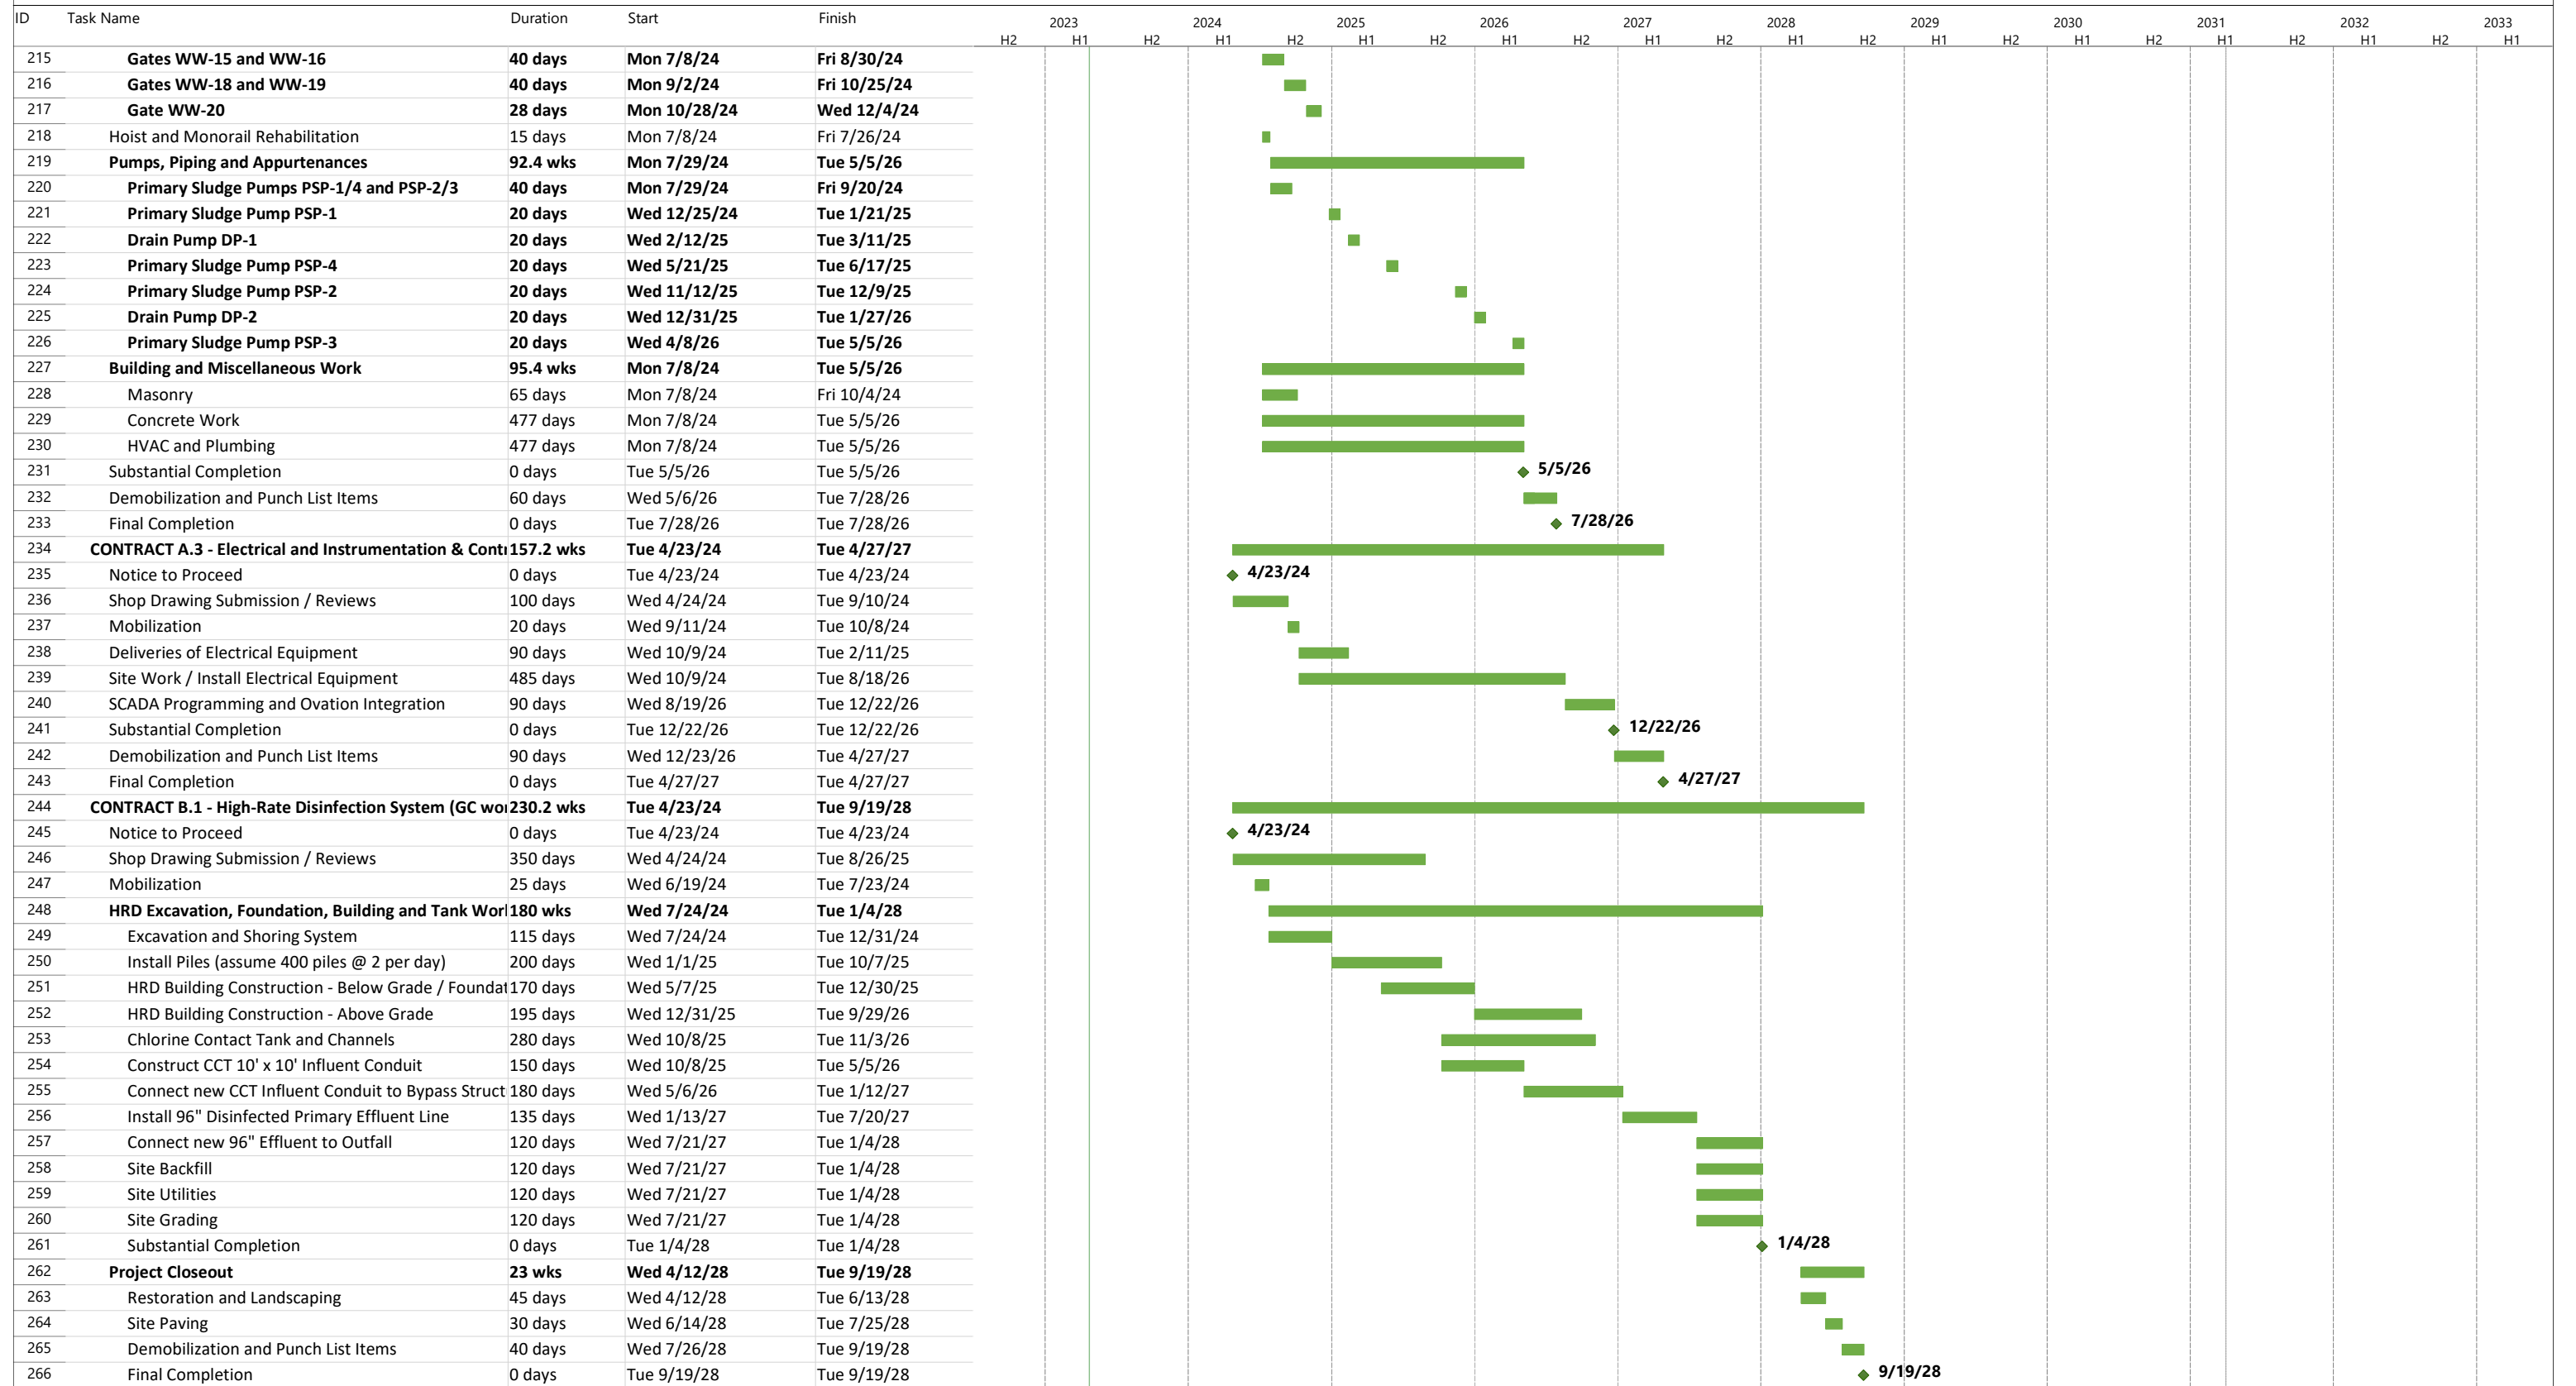

Project: BSA_SchedulePhase1_R
 Date: Mon 4/24/23

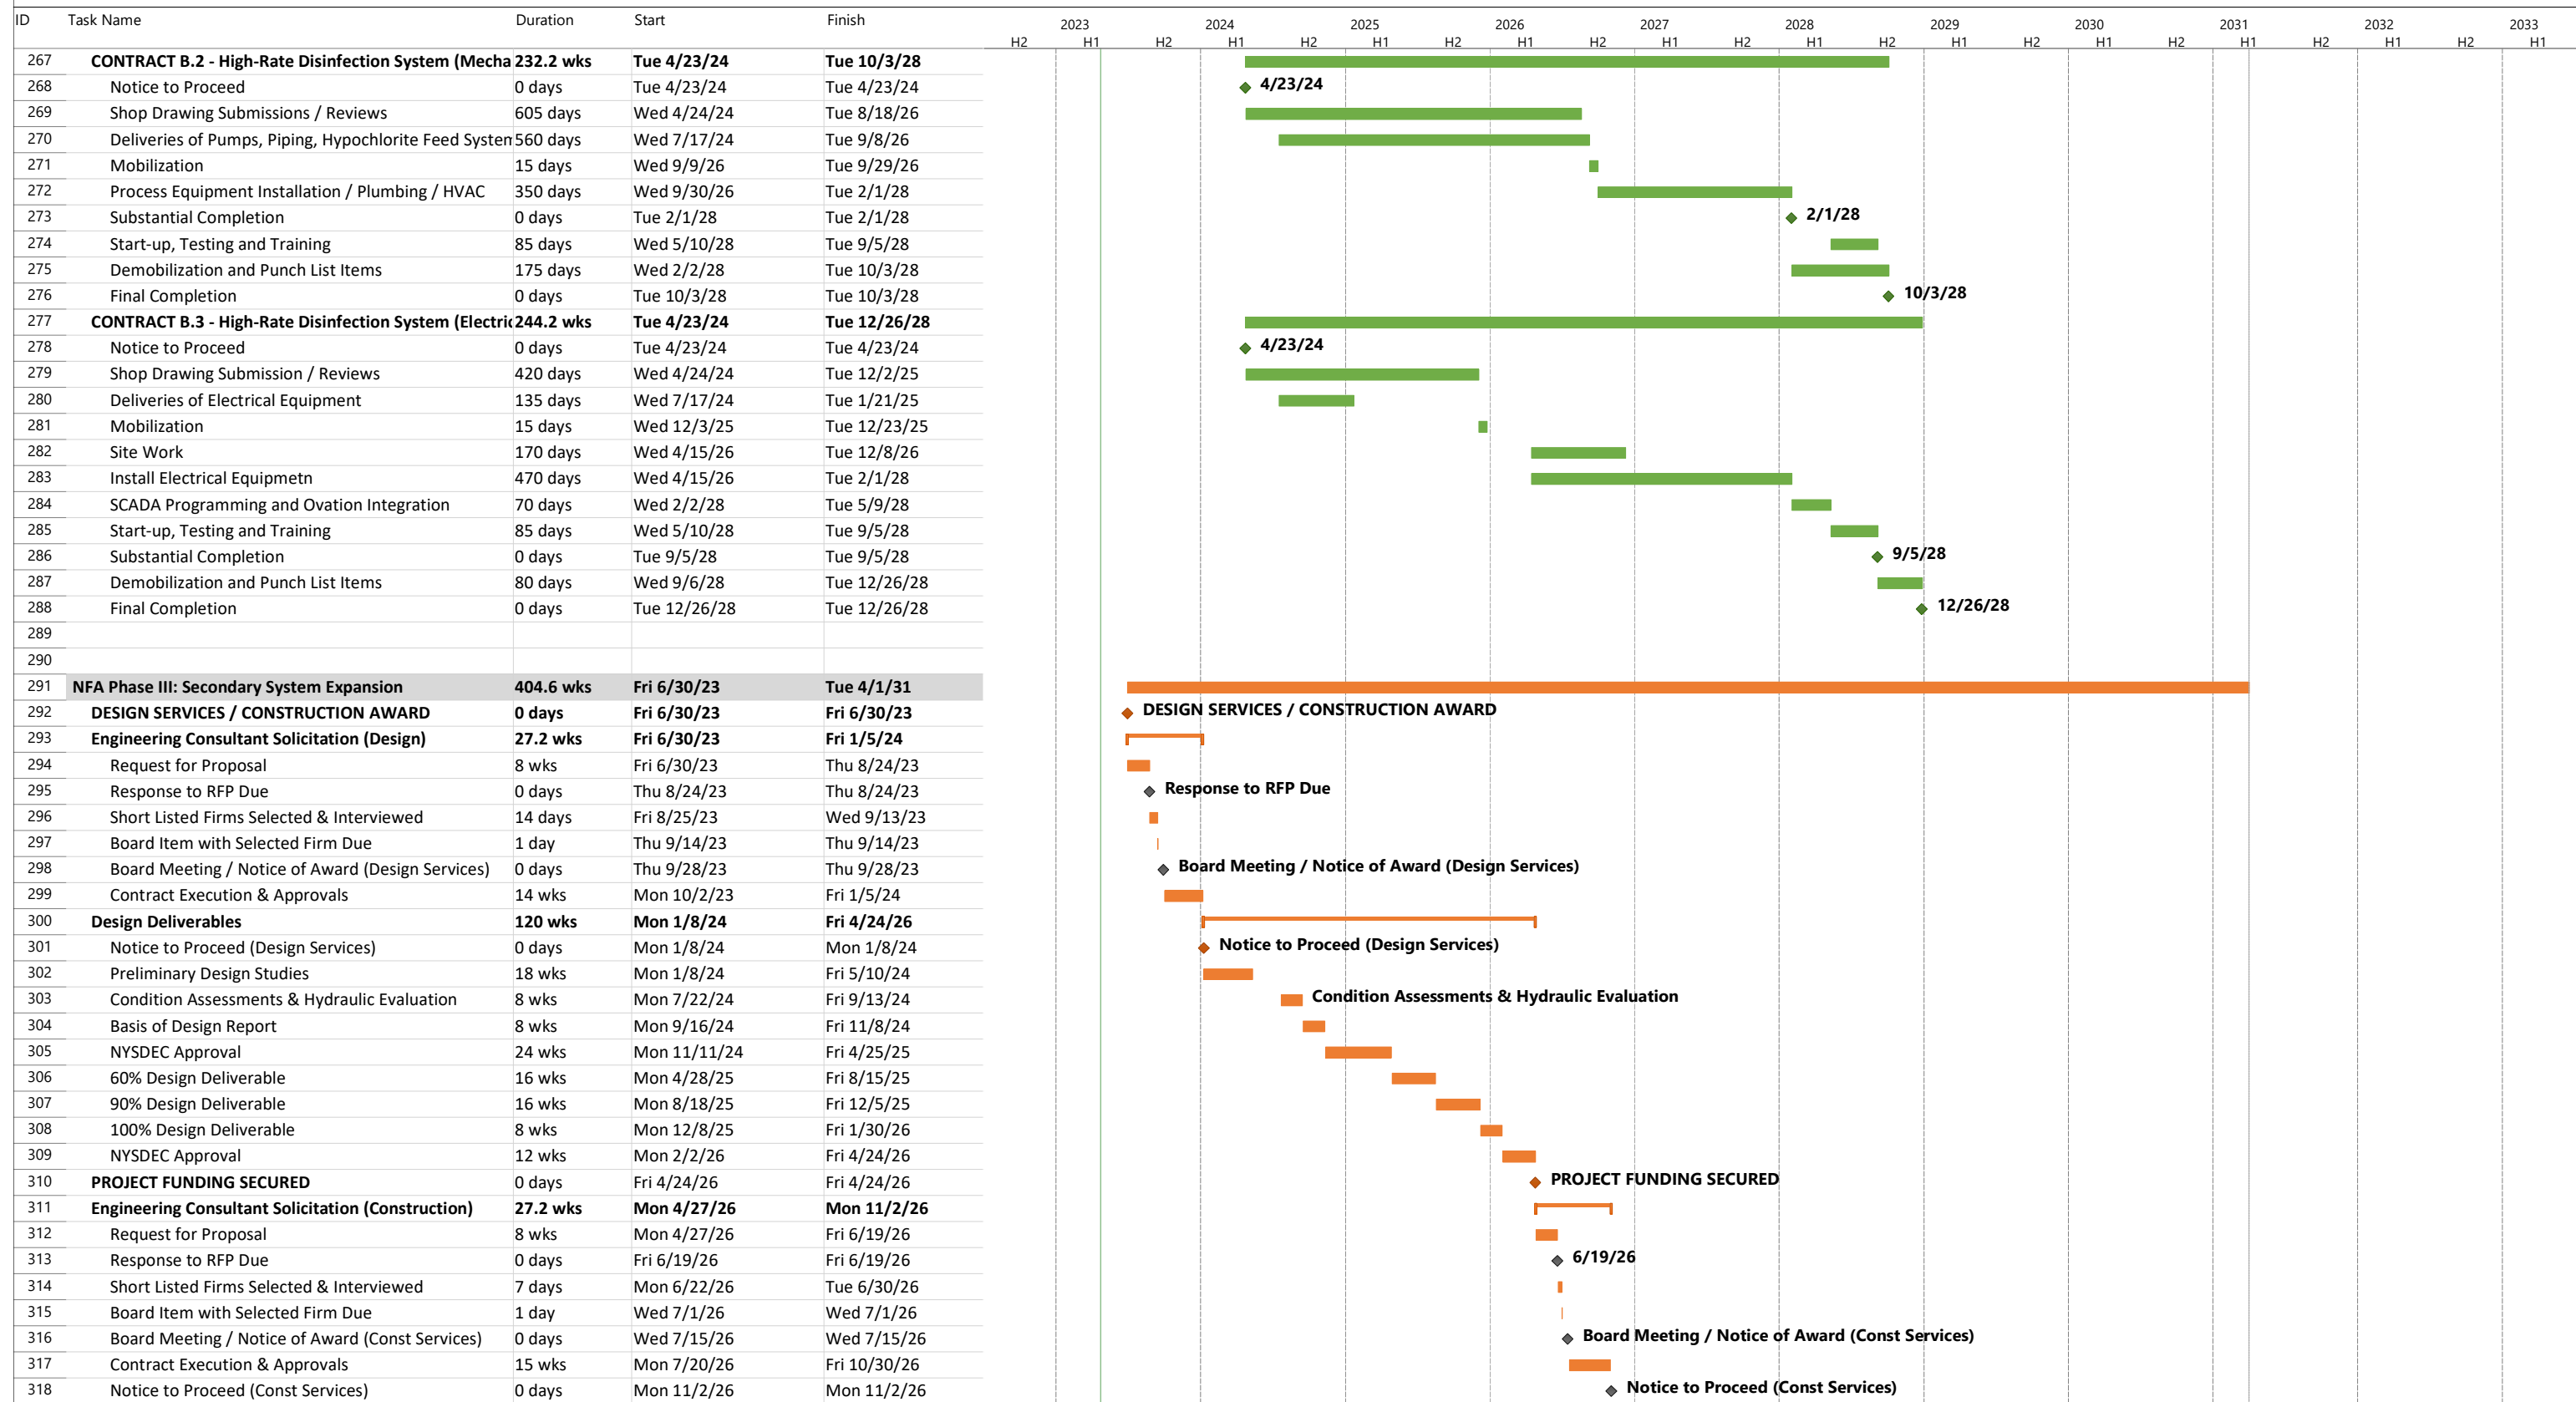

Project: BSA_SchedulePhase1_R
 Date: Mon 4/24/23

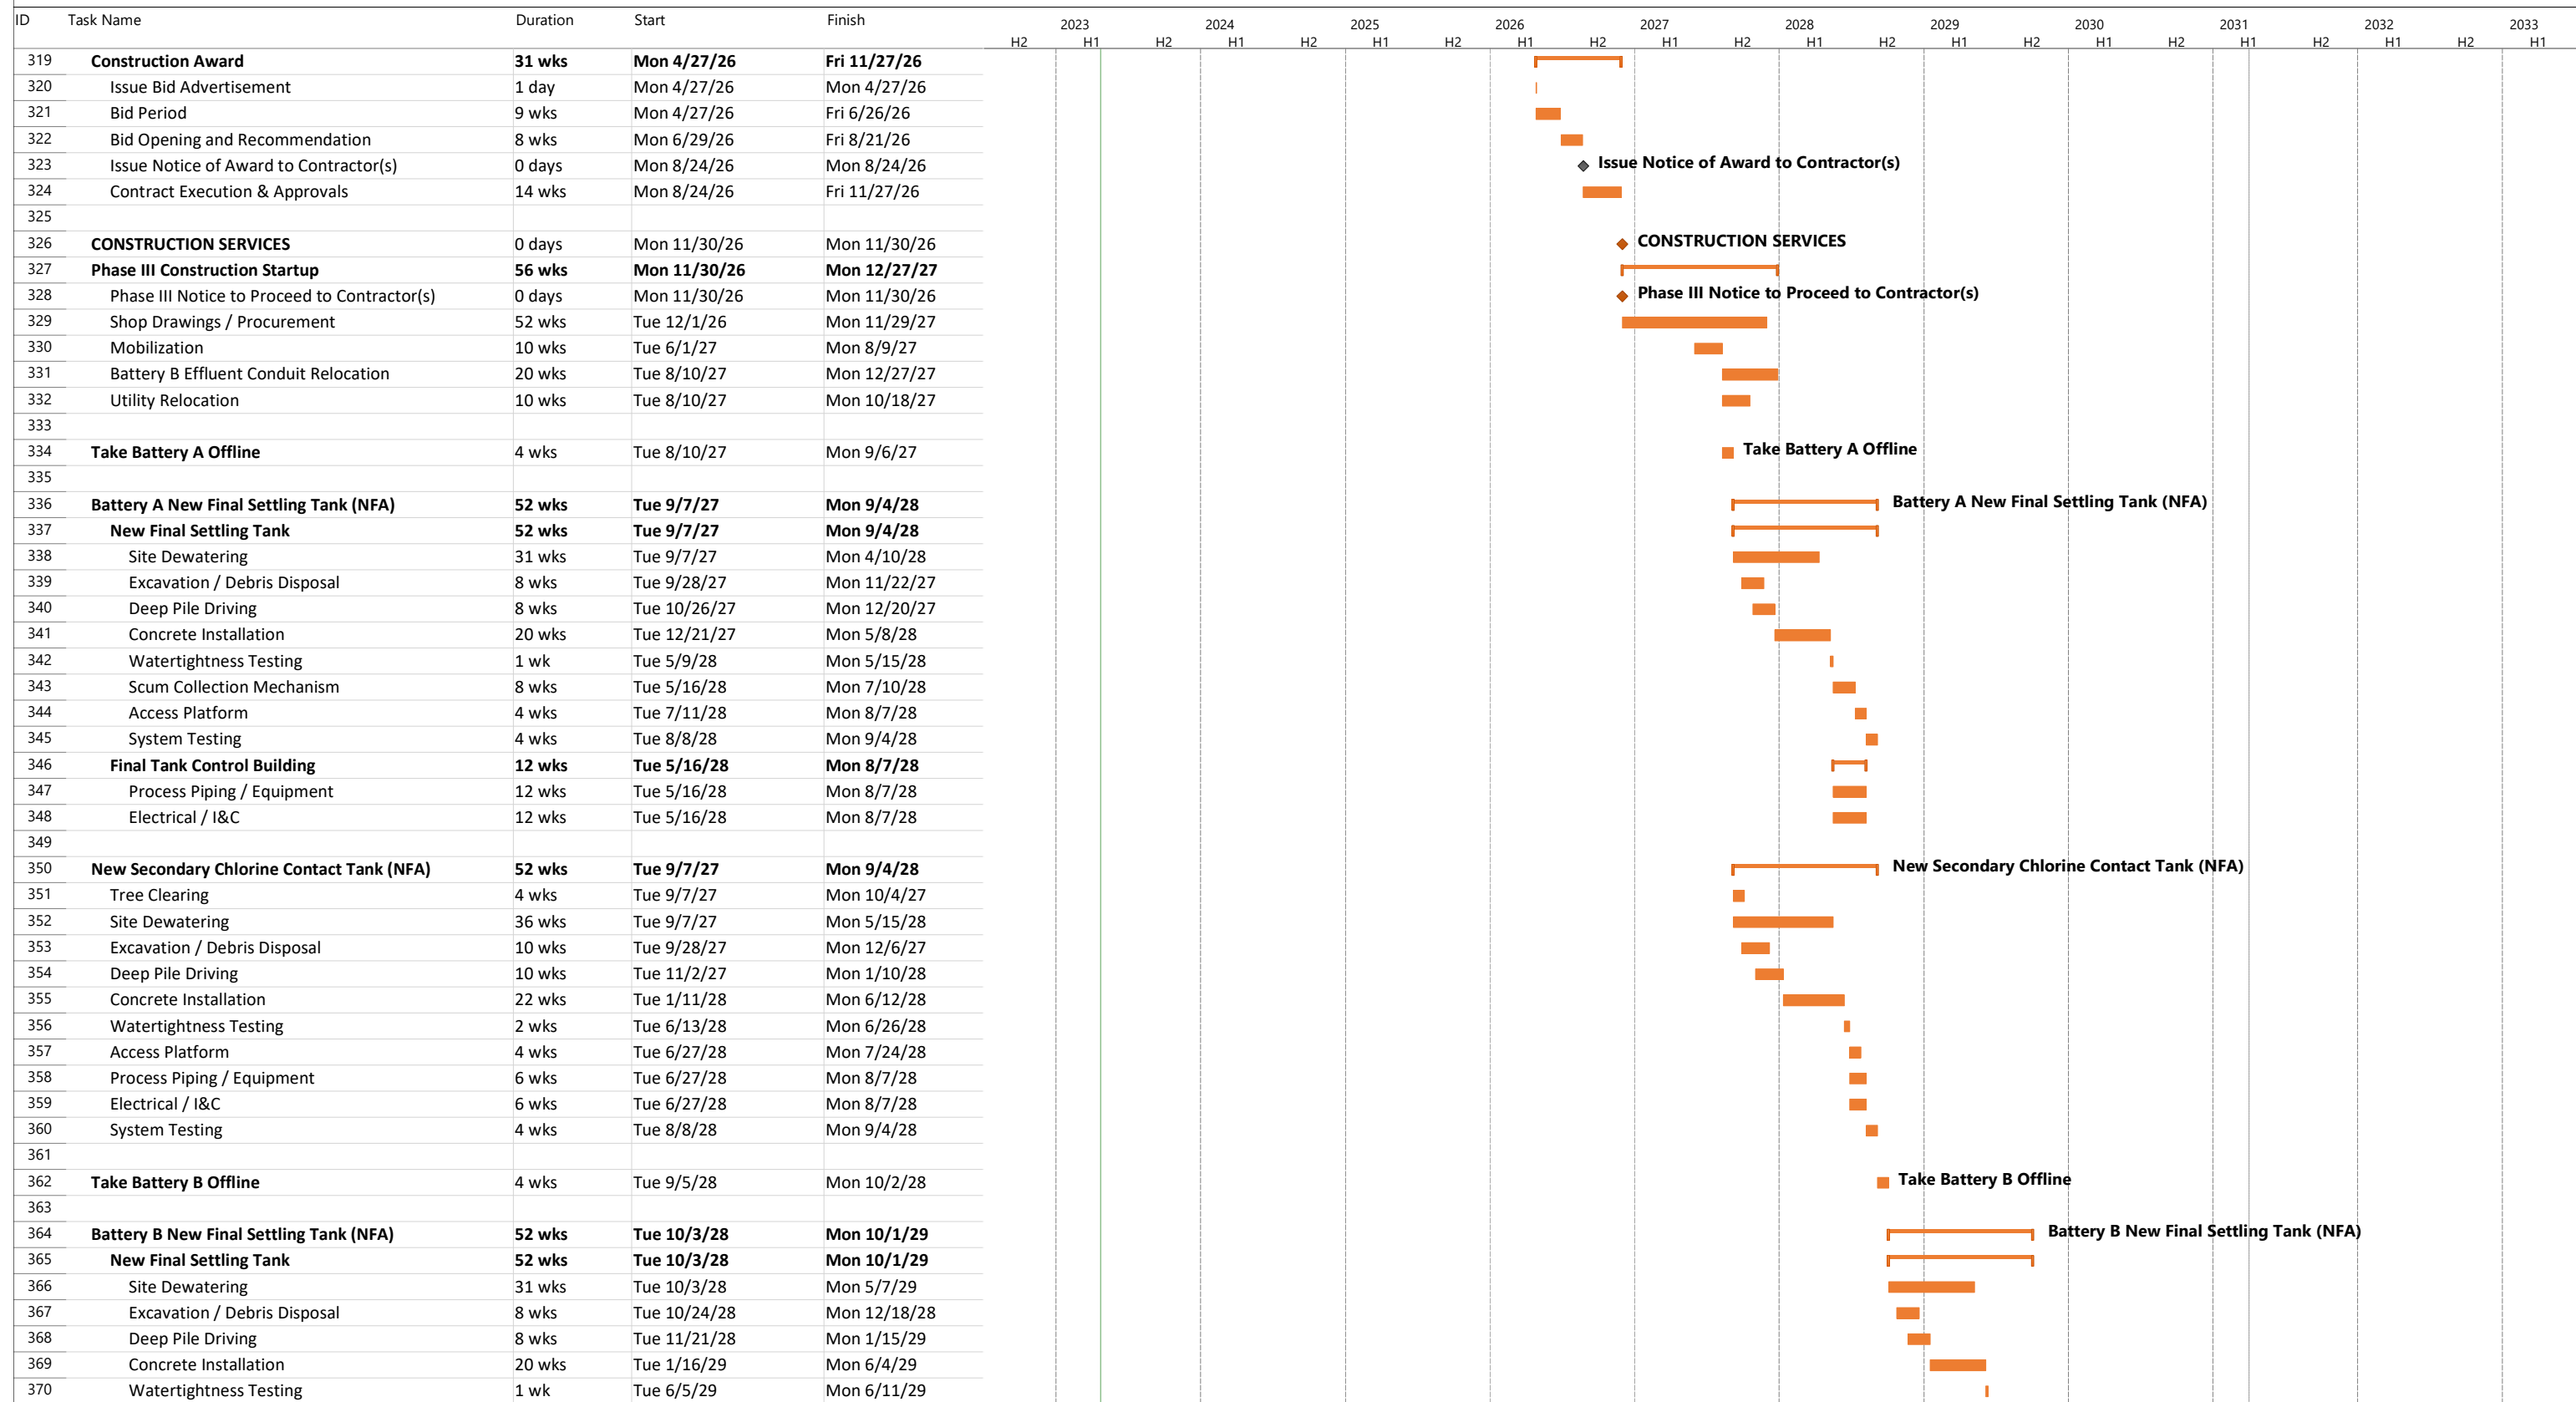

Project: BSA_SchedulePhase1_R
 Date: Mon 4/24/23

ID	Task Name	Duration	Start	Finish	2023		2024		2025		2026		2027		2028		2029		2030		2031		2032		2033	
					H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
371	Scum Collection Mechanism	8 wks	Tue 6/12/29	Mon 8/6/29																						
372	Access Platform	4 wks	Tue 8/7/29	Mon 9/3/29																						
373	System Testing	4 wks	Tue 9/4/29	Mon 10/1/29																						
374	Final Tank Control Building	12 wks	Tue 6/12/29	Mon 9/3/29																						
375	Process Piping / Equipment	12 wks	Tue 6/12/29	Mon 9/3/29																						
376	Electrical / I&C	12 wks	Tue 6/12/29	Mon 9/3/29																						
377																										
378	Battery A FST Rehabilitation (NFA)	40 wks	Tue 8/10/27	Mon 5/15/28																						
379	Setup Dewatering Facility	4 wks	Tue 8/10/27	Mon 9/6/27																						
380	Final Settling Tank Nos. 1, 2	32 wks	Tue 9/7/27	Mon 4/17/28																						
381	Building Process Mechanical / Electrical / I&C Imprc	16 wks	Tue 9/7/27	Mon 12/27/27																						
382	Tank Isolation / Dewatering	4 wks	Tue 12/28/27	Mon 1/24/28																						
383	Tank Cleaning / Debris Disposal	6 wks	Tue 1/25/28	Mon 3/6/28																						
384	Concrete Repairs	7 wks	Tue 2/15/28	Mon 4/3/28																						
385	Influent Trough Orifice Modifications	2 wks	Tue 2/22/28	Mon 3/6/28																						
386	Influent / Effluent Trough Wall Extension	4 wks	Tue 3/7/28	Mon 4/3/28																						
387	System Testing	2 wks	Tue 4/4/28	Mon 4/17/28																						
388	Final Settling Tank Nos. 3, 4	32 wks	Tue 8/10/27	Mon 3/20/28																						
389	Building Process Mechanical / Electrical / I&C Imprc	16 wks	Tue 8/10/27	Mon 11/29/27																						
390	Tank Isolation / Dewatering	4 wks	Tue 11/30/27	Mon 12/27/27																						
391	Tank Cleaning / Debris Disposal	6 wks	Tue 12/28/27	Mon 2/7/28																						
392	Concrete Repairs	7 wks	Tue 1/18/28	Mon 3/6/28																						
393	Influent Trough Orifice Modifications	2 wks	Tue 1/25/28	Mon 2/7/28																						
394	Influent / Effluent Trough Wall Extension	4 wks	Tue 2/8/28	Mon 3/6/28																						
395	System Testing	2 wks	Tue 3/7/28	Mon 3/20/28																						
396	Final Settling Tank Nos. 5, 6, 7, 8	40 wks	Tue 8/10/27	Mon 5/15/28																						
397	Building Process Mechanical / Electrical / I&C Imprc	20 wks	Tue 8/10/27	Mon 12/27/27																						
398	Tank Isolation / Dewatering	4 wks	Tue 12/28/27	Mon 1/24/28																						
399	Tank Cleaning / Debris Disposal	8 wks	Tue 1/25/28	Mon 3/20/28																						
400	Concrete Repairs	6 wks	Tue 3/7/28	Mon 4/17/28																						
401	Influent Trough Orifice Modifications	4 wks	Tue 3/7/28	Mon 4/3/28																						
402	Influent / Effluent Trough Wall Extension	6 wks	Tue 3/7/28	Mon 4/17/28																						
403	System Testing	4 wks	Tue 4/18/28	Mon 5/15/28																						
404																										
405	Battery B FST Rehabilitation (NFA)	40 wks	Tue 10/3/28	Mon 7/9/29																						
406	Setup Dewatering Facility	4 wks	Tue 10/3/28	Mon 10/30/28																						
407	Final Settling Tank Nos. 1, 2	32 wks	Tue 10/3/28	Mon 5/14/29																						
408	Building Process Mechanical / Electrical / I&C Imprc	16 wks	Tue 10/3/28	Mon 1/22/29																						
409	Tank Isolation / Dewatering	4 wks	Tue 1/23/29	Mon 2/19/29																						
410	Tank Cleaning / Debris Disposal	6 wks	Tue 2/20/29	Mon 4/2/29																						
411	Concrete Repairs	7 wks	Tue 3/13/29	Mon 4/30/29																						
412	Influent Trough Orifice Modifications	2 wks	Tue 3/20/29	Mon 4/2/29																						
413	Influent / Effluent Trough Wall Extension	4 wks	Tue 4/3/29	Mon 4/30/29																						
414	System Testing	2 wks	Tue 5/1/29	Mon 5/14/29																						
415	Final Settling Tank Nos. 3, 4	32 wks	Tue 10/3/28	Mon 5/14/29																						
416	Building Process Mechanical / Electrical / I&C Imprc	16 wks	Tue 10/3/28	Mon 1/22/29																						
417	Tank Isolation / Dewatering	4 wks	Tue 1/23/29	Mon 2/19/29																						
418	Tank Cleaning / Debris Disposal	6 wks	Tue 2/20/29	Mon 4/2/29																						
419	Concrete Repairs	7 wks	Tue 3/13/29	Mon 4/30/29																						
420	Influent Trough Orifice Modifications	2 wks	Tue 3/20/29	Mon 4/2/29																						
421	Influent / Effluent Trough Wall Extension	4 wks	Tue 4/3/29	Mon 4/30/29																						
422	System Testing	2 wks	Tue 5/1/29	Mon 5/14/29																						

